


# TALEGA

## 2025 NEIGHBORHOOD CONSTRUCTION SCHEDULE

JUNE 9 - AUGUST 7  
(WEATHER PERMITTING)

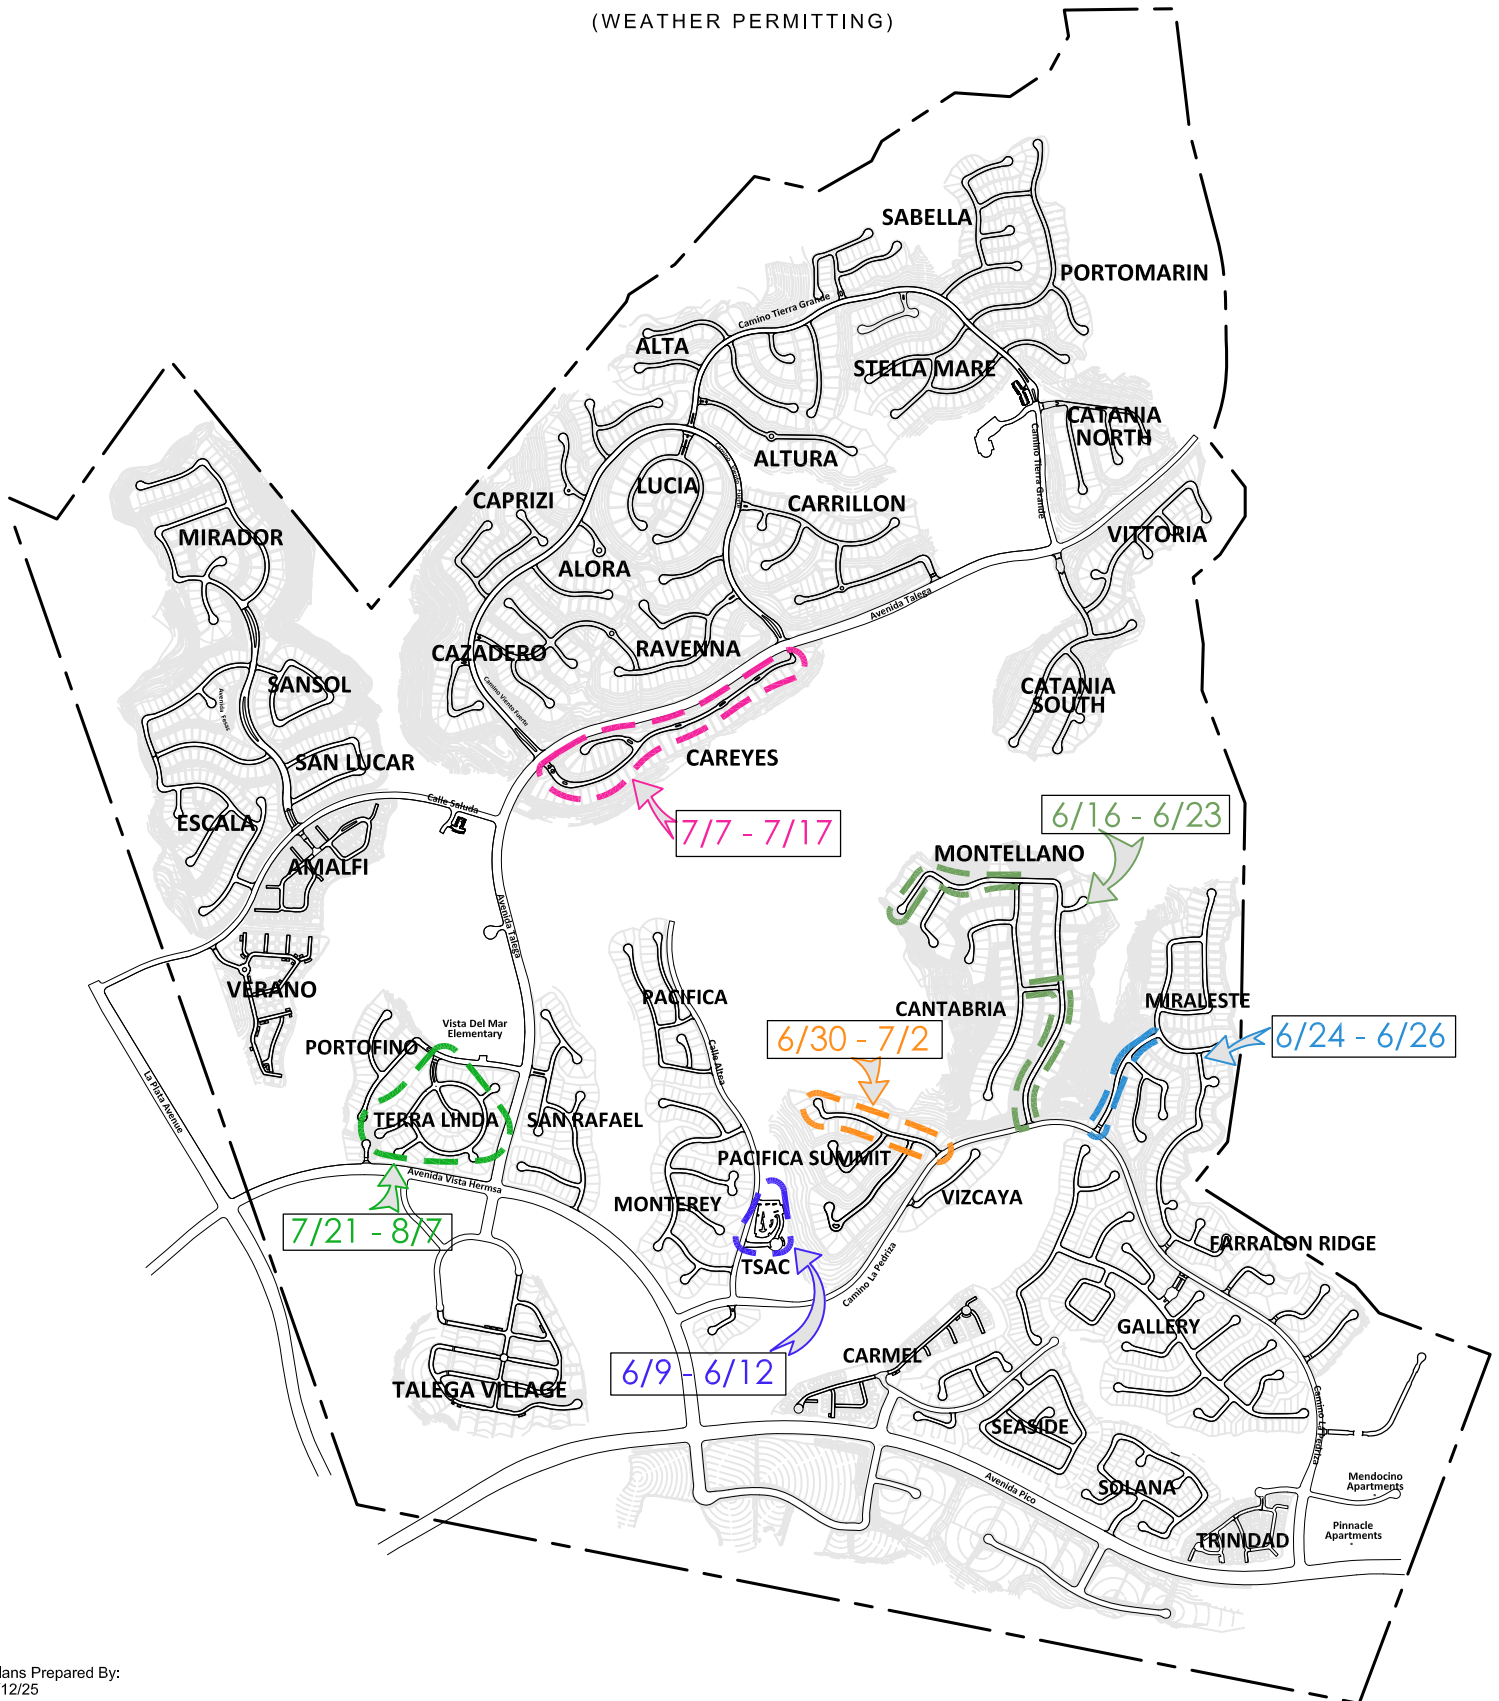

Plans Prepared By:  
5/12/25



Project Engineer:  
LaBelle Marvin, Inc.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

PAVING CONTRACTOR  
CHAMPION PAVING

# TALGA SWIM AND ATHLETIC CLUB

## 2025 PARKING LOT CONSTRUCTION SCHEDULE


TALEGA MAINTENANCE CORPORATION

JUNE 9 - JUNE 13

(WEATHER PERMITTING)


FRIDAY 6/13 - PARKING LOT CLOSED


6/11 - 6/12

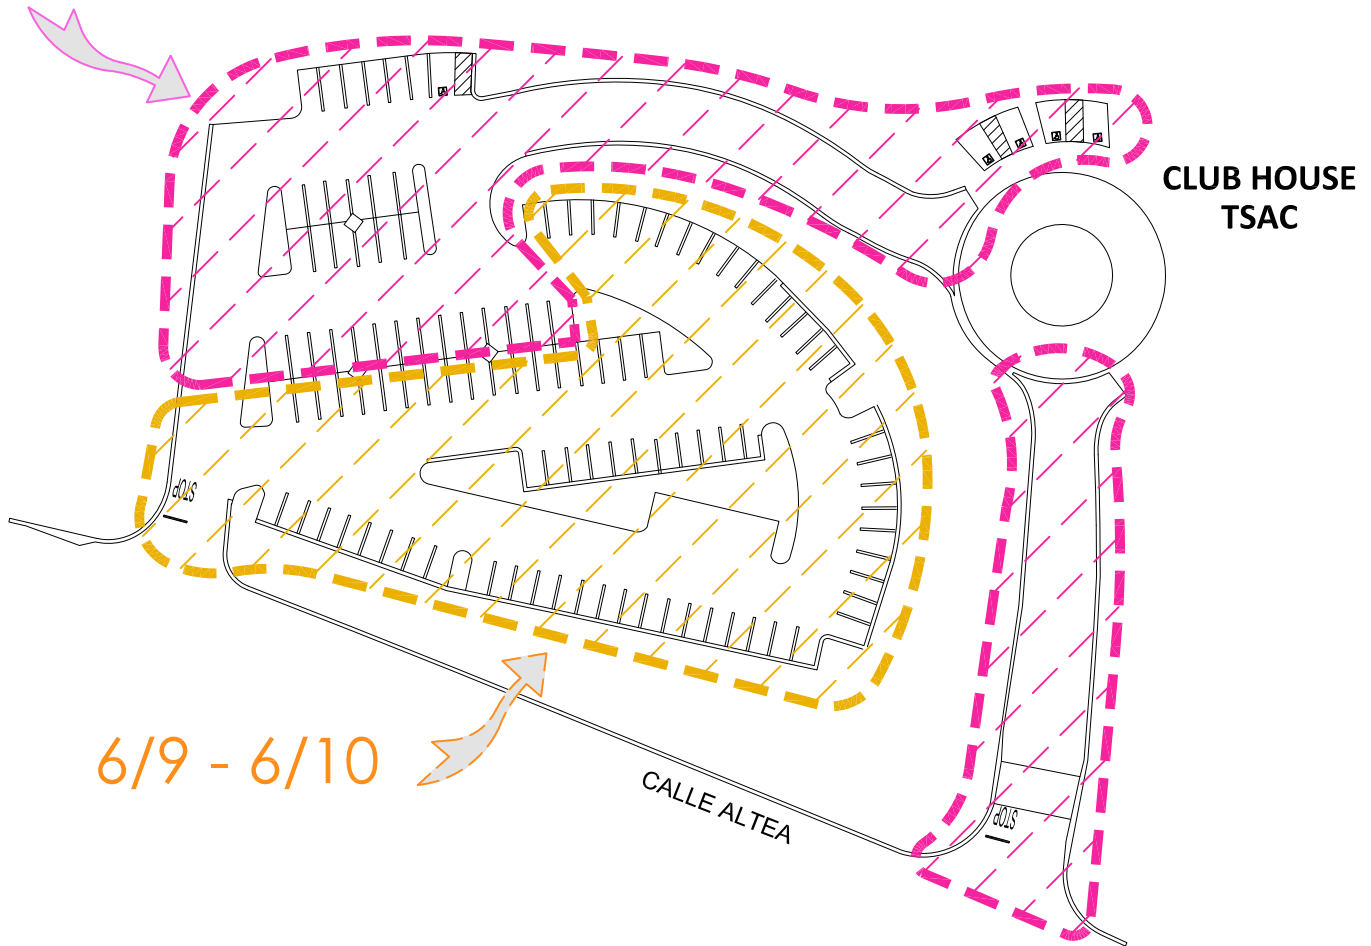

## PARKING LOT CLOSURES

### STREET REPAIR SCHEDULE

 6/9 - 6/10

 6/11 - 6/12

FRIDAY 6/13 - PARKING LOT CLOSED

### TRASH DAYS

JUNE 9

TRASH SHALL BE  
PICKED UP EARLY  
MORNING

Plans Prepared By:  
6/4/25



Project Engineer:  
LaBelle Marvin, Inc.

Sidewalk access is open During Construction

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

PAVING CONTRACTOR  
CHAMPION PAVING

# MONTELLANO

## 2025 STREET CONSTRUCTION SCHEDULE

TALEGA MAINTENANCE CORPORATION

JUNE 16 - JUNE 23

(WEATHER PERMITTING)


### STREET CLOSURES



AREA 1	DATE	Daily Work Schedule
MON.	6/16	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	6/17	CLOSED 7:30 AM to 6:00 PM (PAVING)
WED.	6/18	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 2	DATE	Daily Work Schedule
THURS.	6/19	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
FRI.	6/20	CLOSED 7:30 AM to 6:00 PM (PAVING)
MON.	6/22	CLOSED 7:30 AM to 6:00 PM (PAVING)

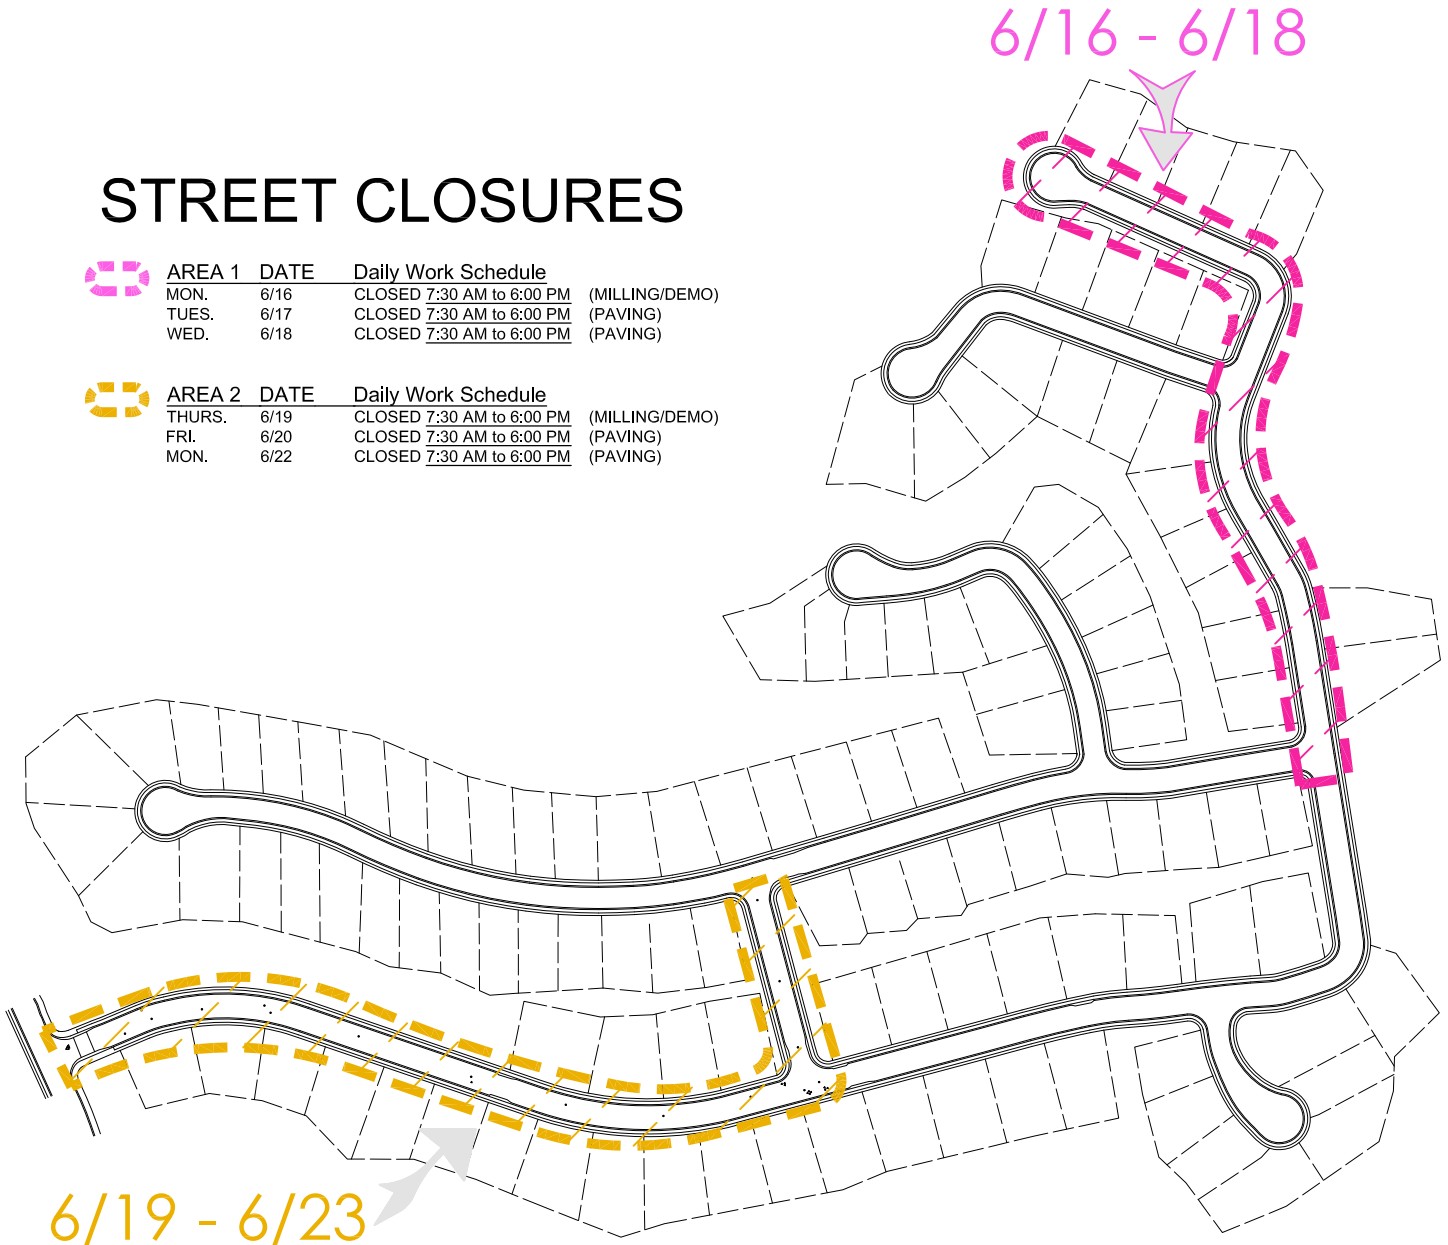

TRAFFIC CONTROL SHALL BE UTILIZED TO  
PERMIT INGRESS/EGRESS DURING  
CONSTRUCTION FROM 6/19 - 6/23

HOWEVER PLEASE BE ADVISED FROM  
7:30 AM TO 6:00 PM POTENTIAL DELAYS  
AND LONG WAITS ANTICIPATED

#### TRASH DAYS

JUNE 18  
TRASH SHALL BE  
PICKED UP EARLY  
MORNING

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

PAVING CONTRACTOR  
CHAMPION PAVING

Plans Prepared By:  
5/12/25



Project Engineer:  
LaBelle Marvin, Inc.


# FARRALON RIDGE

## 2025 STREET CONSTRUCTION SCHEDULE

TALEGA MAINTENANCE CORPORATION

JUNE 24 - JUNE 26

(WEATHER PERMITTING)

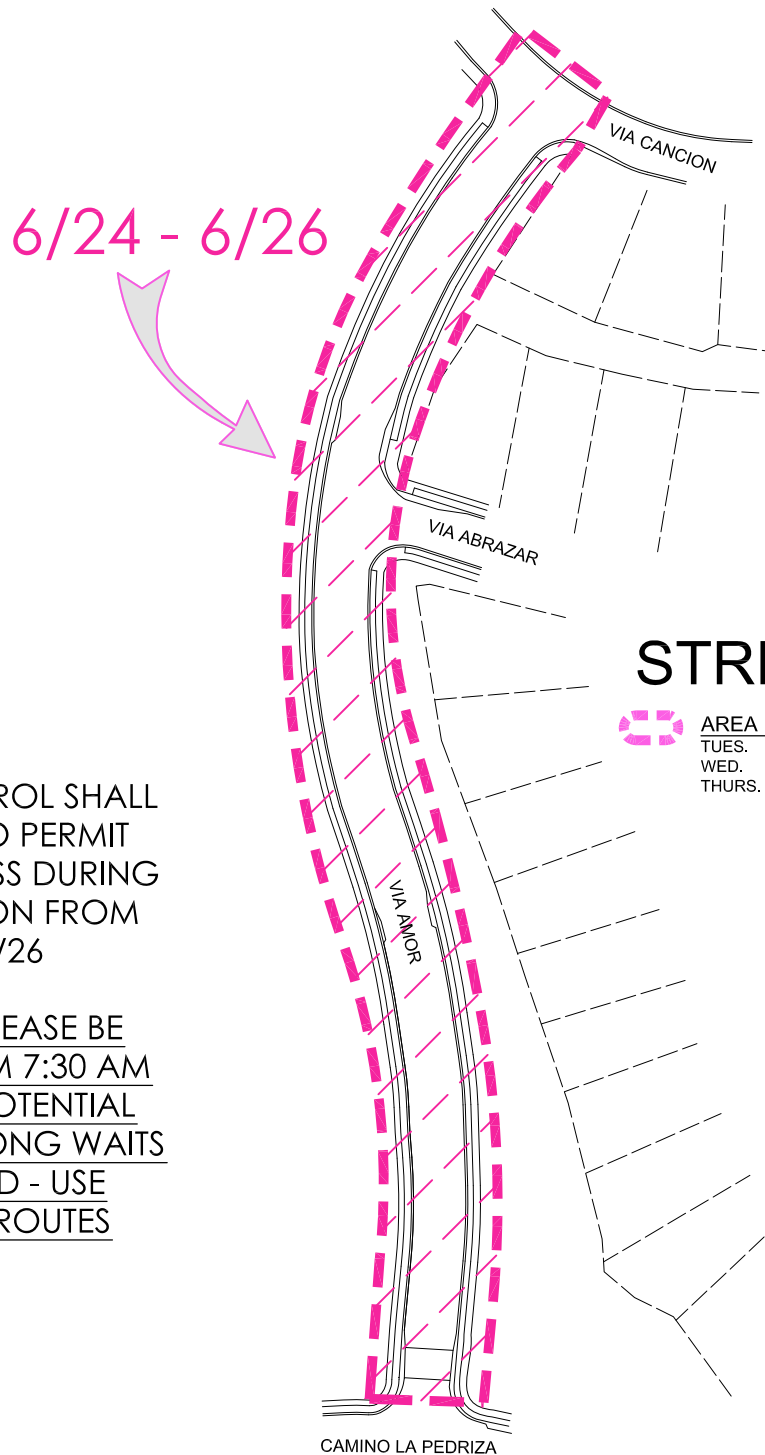

TRAFFIC CONTROL SHALL  
BE UTILIZED TO PERMIT  
INGRESS/EGRESS DURING  
CONSTRUCTION FROM  
6/24 - 6/26

HOWEVER PLEASE BE  
ADVISED FROM 7:30 AM  
TO 6:00 PM POTENTIAL  
DELAYS AND LONG WAITS  
ANTICIPATED - USE  
ALTERNATE ROUTES

## STREET CLOSURES



AREA 1	DATE	Daily Work Schedule	
TUES.	6/24	CLOSED 7:30 AM to 5:00 PM	(MILLING/DEMO)
WED.	6/25	CLOSED 7:30 AM to 5:00 PM	(PAVING)
THURS.	6/26	CLOSED 7:30 AM to 5:00 PM	(PAVING)

### TRASH DAYS

JUNE 25  
NO TRASH PICK-UP  
DUE TO ROAD  
CONSTRUCTION

TRASH PICK UP SHALL  
RESUME JULY 2

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

Plans Prepared By:  
6/4/25



Project Engineer:  
LaBelle Marvin, Inc.

PAVING CONTRACTOR  
CHAMPION PAVING

# PACIFIC SUMMIT

## 2025 STREET CONSTRUCTION SCHEDULE


TALEGA MAINTENANCE CORPORATION

JUNE 30 - JULY 2

(WEATHER PERMITTING)

TRAFFIC CONTROL SHALL  
BE UTILIZED TO PERMIT  
INGRESS/EGRESS DURING  
CONSTRUCTION FROM  
6/30 - 7/2

HOWEVER PLEASE BE  
ADVISED FROM 7:30 AM  
TO 6:00 PM POTENTIAL  
DELAYS AND LONG WAITS  
ANTICIPATED

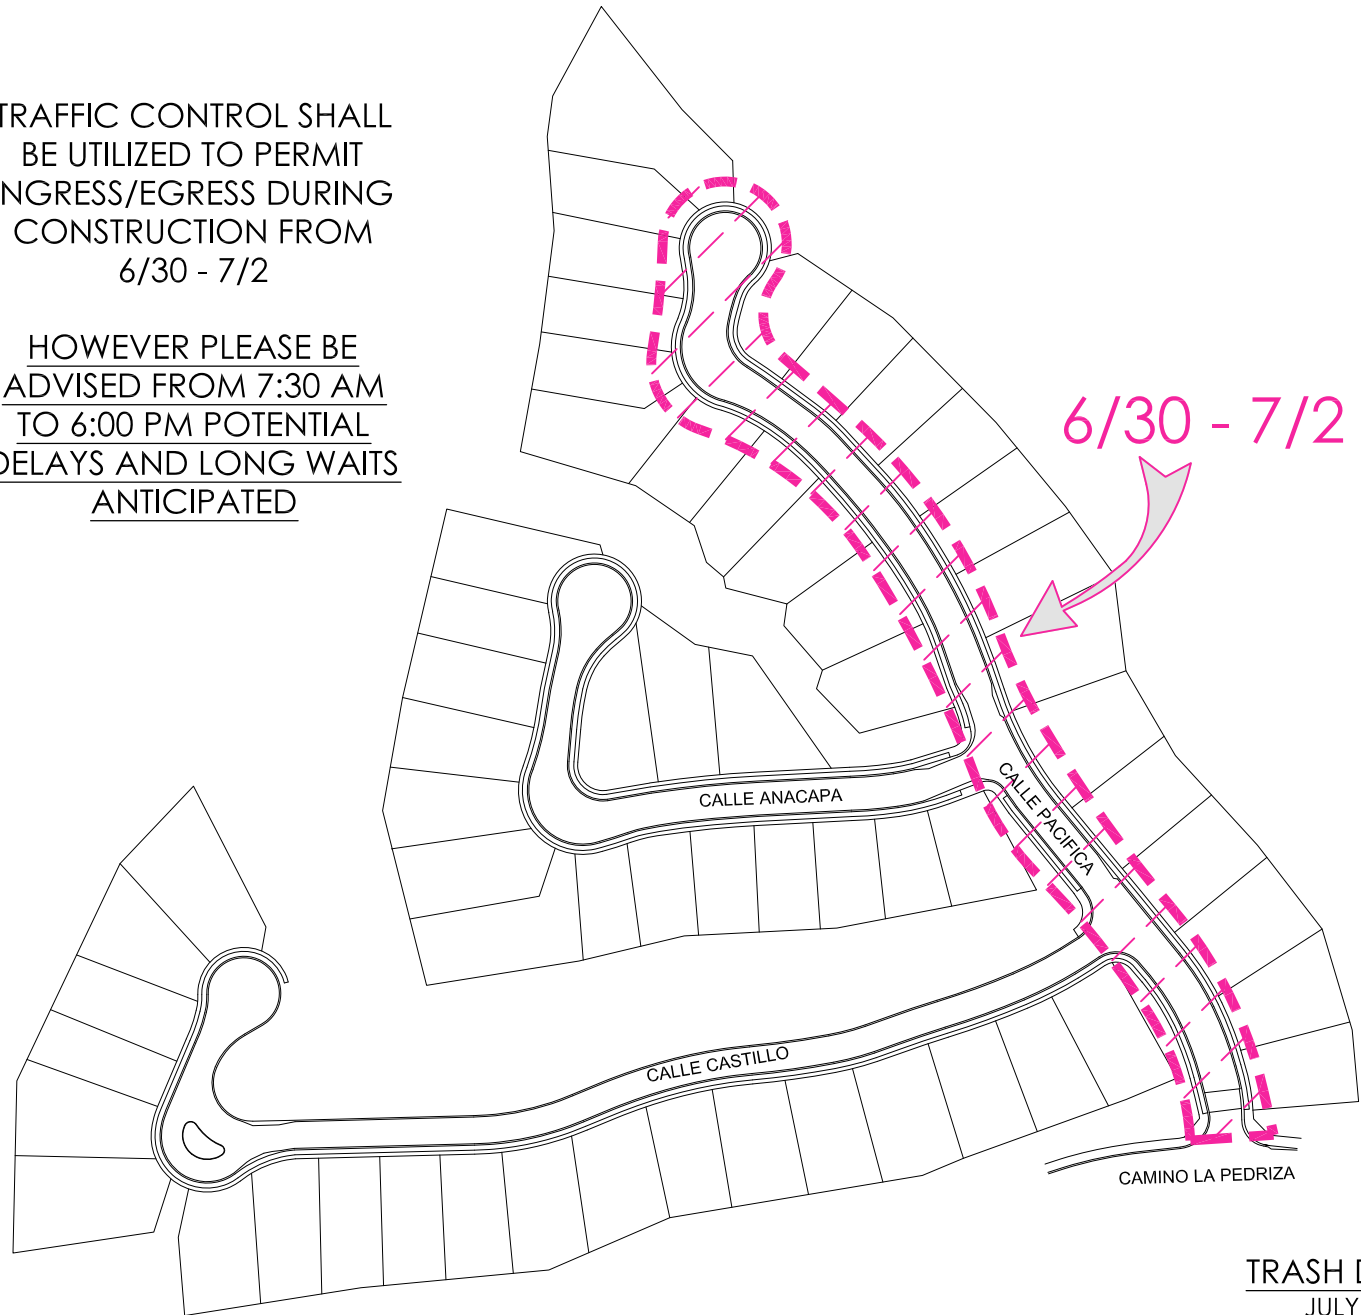

## STREET CLOSURES



AREA 1	DATE	Daily Work Schedule
MON.	6/30	CLOSED 7:30 AM to 5:00 PM (MILLING/DEMO)
TUES.	7/1	CLOSED 7:30 AM to 5:00 PM (PAVING)
WED.	7/2	CLOSED 7:30 AM to 5:00 PM (PAVING)

### TRASH DAYS

JULY 2

TRASH SHALL BE  
PICKED UP EARLY  
MORNING

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

Plans Prepared By:  
5/12/25



Project Engineer:  
LaBelle Marvin, Inc.

PAVING CONTRACTOR  
CHAMPION PAVING



# CAREYES

## 2025 STREET CONSTRUCTION SCHEDULE

TALEGA MAINTENANCE CORPORATION

JULY 7 - JULY 17

(WEATHER PERMITTING)

### STREET CLOSURES




AREA 1	DATE	Daily Work Schedule
MON.	7/7	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	7/8	CLOSED 7:30 AM to 6:00 PM (PAVING)
WED.	7/9	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 2	DATE	Daily Work Schedule
THURS.	7/10	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
FRI.	7/11	CLOSED 7:30 AM to 6:00 PM (PAVING)
MON.	7/14	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 3	DATE	Daily Work Schedule
TUES.	7/15	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
WED.	7/16	CLOSED 7:30 AM to 6:00 PM (PAVING)
THURS.	7/17	CLOSED 7:30 AM to 6:00 PM (PAVING)

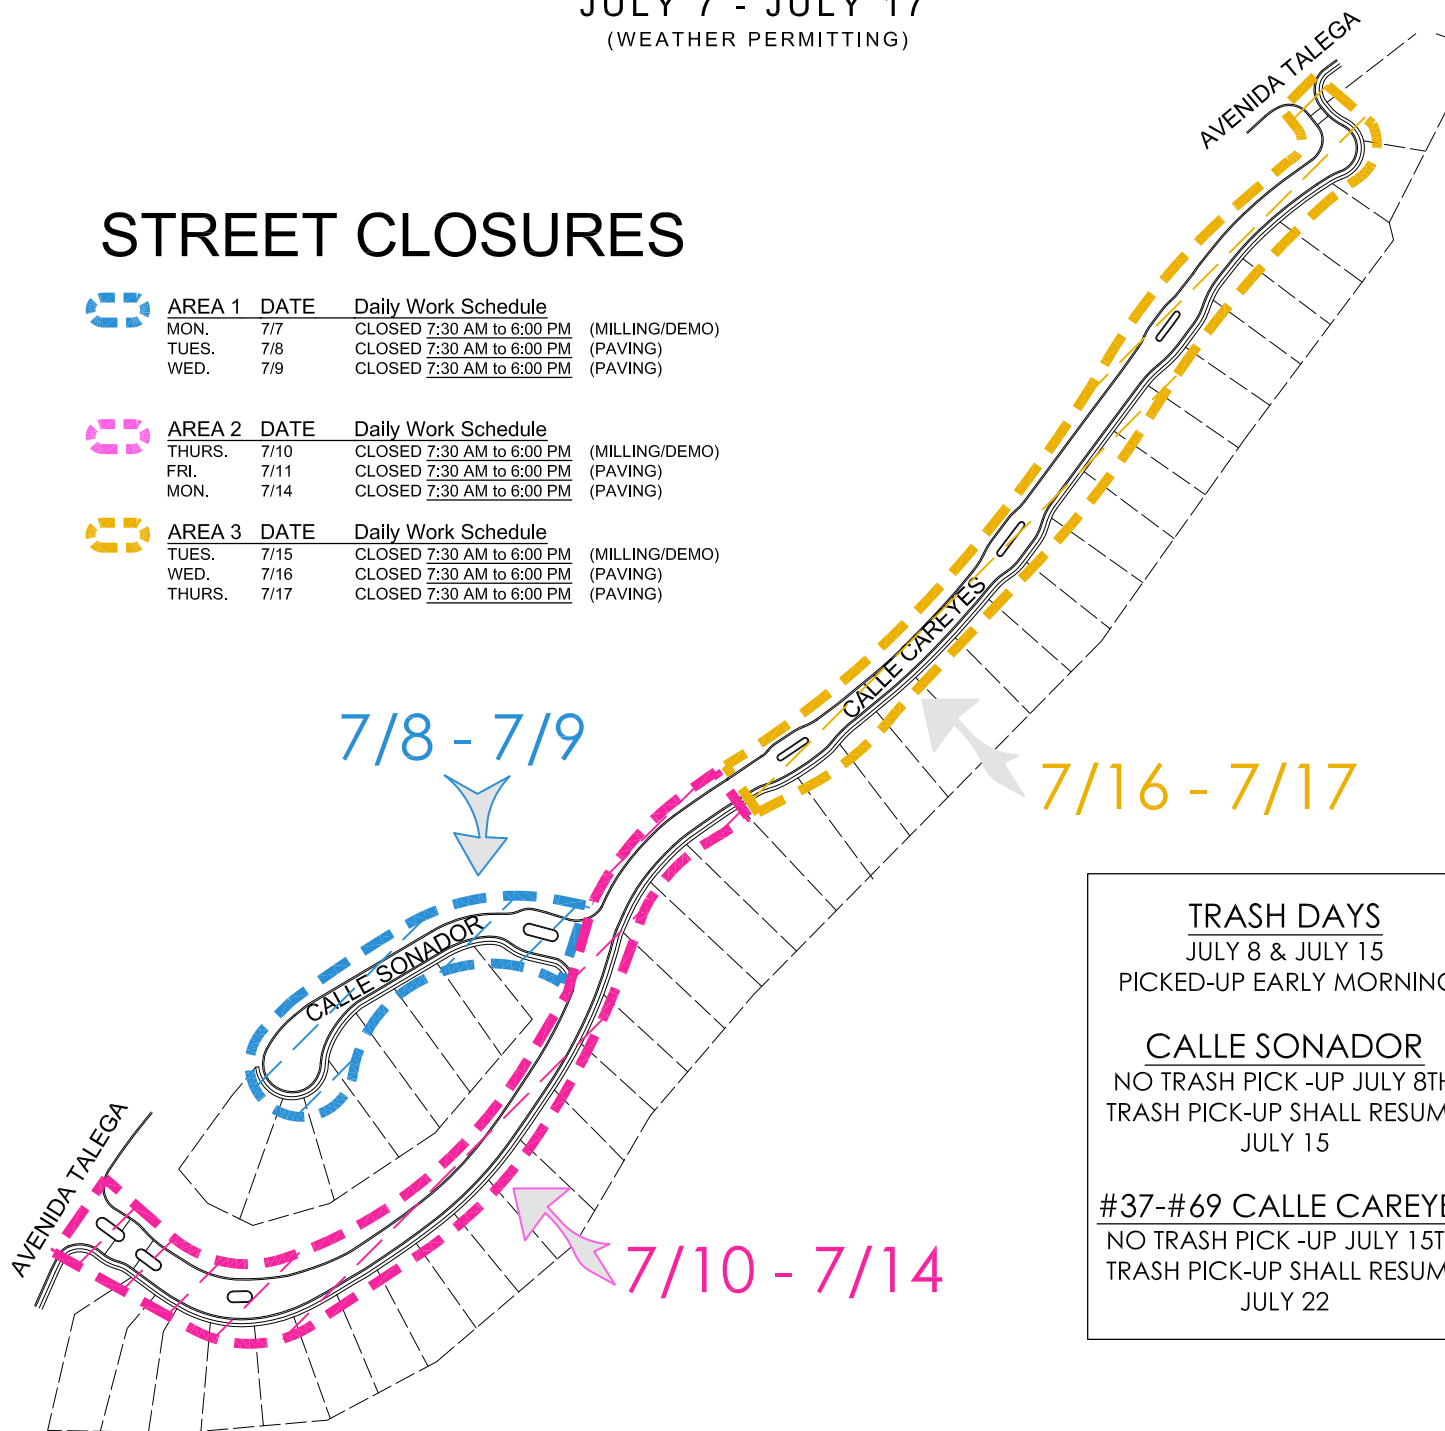

#### TRASH DAYS

JULY 8 & JULY 15

PICKED-UP EARLY MORNING

#### CALLE SONADOR

NO TRASH PICK-UP JULY 8TH  
TRASH PICK-UP SHALL RESUME  
JULY 15

#### #37-#69 CALLE CAREYES

NO TRASH PICK-UP JULY 15TH  
TRASH PICK-UP SHALL RESUME  
JULY 22

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

Plans Prepared By:  
6/4/25



Project Engineer:  
LaBelle Marvin, Inc.

PAVING CONTRACTOR  
CHAMPION PAVING

# TERRA LINDA

## 2025 STREET CONSTRUCTION SCHEDULE

TALEGA MAINTENANCE CORPORATION

**JULY 21 - AUGUST 7**


(WEATHER PERMITTING)

### TRASH DAYS

JULY 22, JULY 29 AND AUG 5  
PICKED-UP EARLY MORNING

CALLE LOS CORALES,  
PLAZA VIA SOL, PLAZA  
CABANA, #100-104 VIA  
MALAGA

NO TRASH PICK-UP JULY 22ND  
TRASH PICK-UP SHALL RESUME  
JULY 29 AND AUG 5

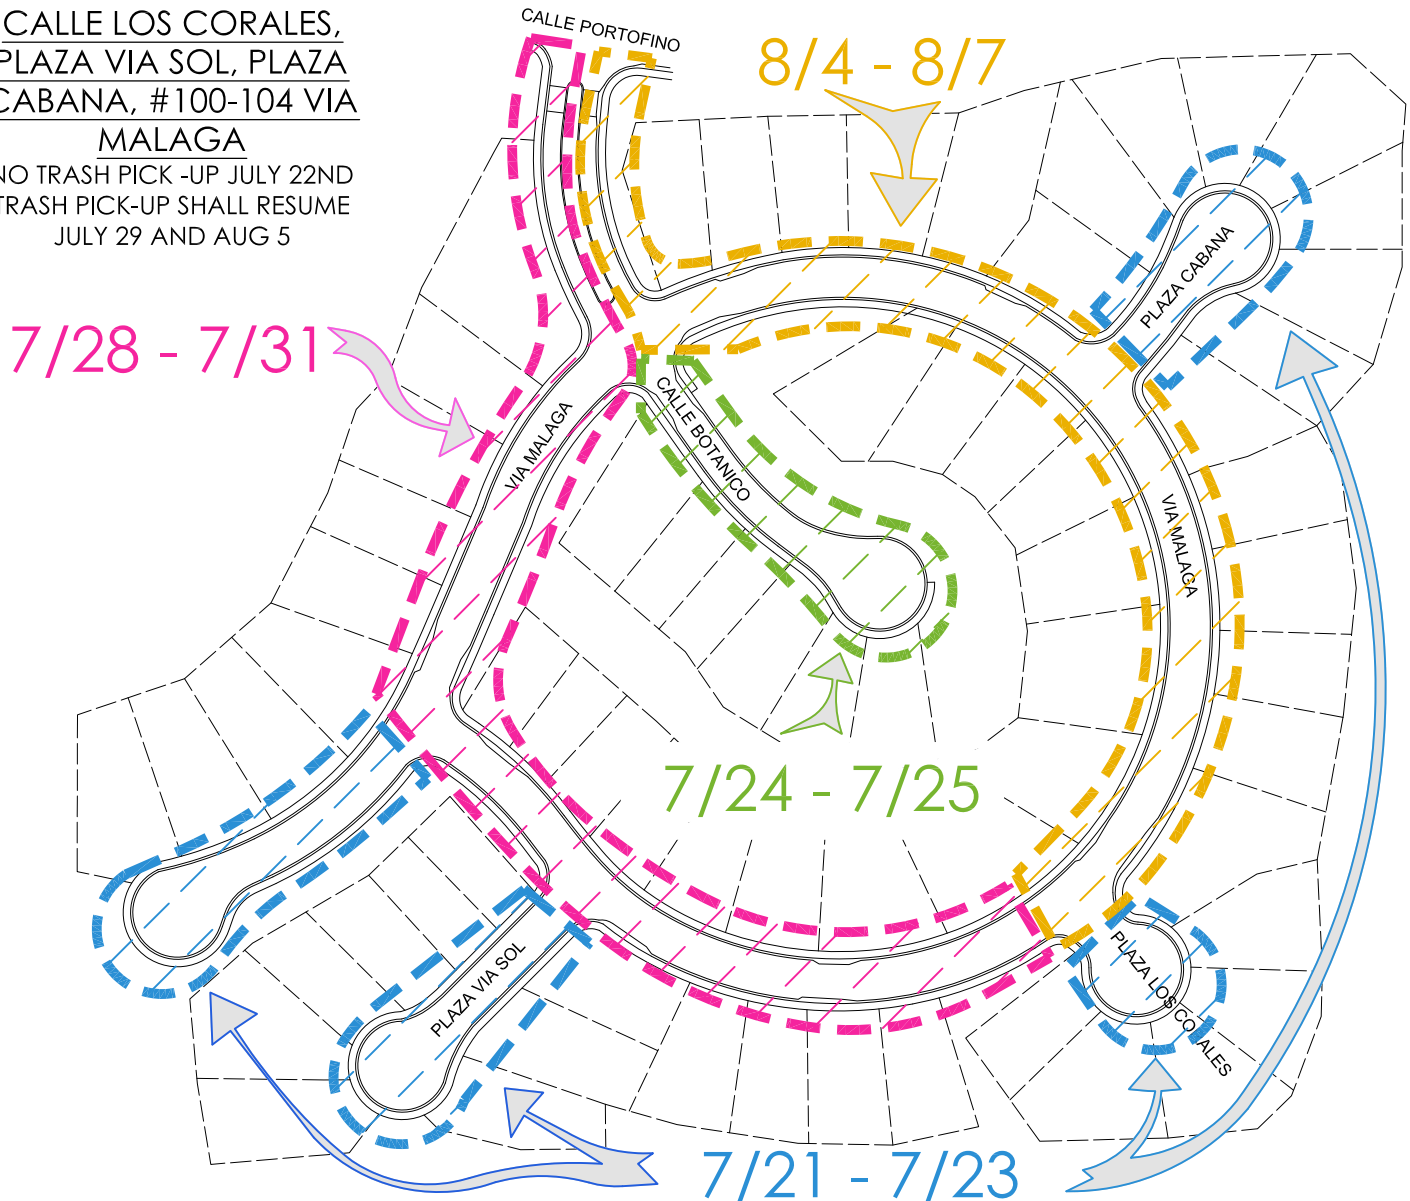

## STREET CLOSURES



AREA 1	DATE	Daily Work Schedule
MON.	7/21	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	7/22	CLOSED 7:30 AM to 6:00 PM (PAVING)
WED.	7/23	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 2	DATE	Daily Work Schedule
THURS.	7/24	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
FRI.	7/25	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 3	DATE	Daily Work Schedule
MON.	7/28	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	7/29	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
WED.	7/30	CLOSED 7:30 AM to 6:00 PM (PAVING)
THURS.	7/31	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 4	DATE	Daily Work Schedule
MON.	8/4	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	8/5	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
WED.	8/6	CLOSED 7:30 AM to 6:00 PM (PAVING)
THURS.	8/7	CLOSED 7:30 AM to 6:00 PM (PAVING)

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

**AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE**

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

Plans Prepared By:  
6/4/25



Project Engineer:  
LaBelle Marvin, Inc.

PAVING CONTRACTOR  
**CHAMPION PAVING**
