

TERRA LINDA

2025 STREET CONSTRUCTION SCHEDULE

TALEGA MAINTENANCE CORPORATION

JULY 21 - AUGUST 6

(WEATHER PERMITTING)


TRASH DAYS

JULY 22, JULY 29 AND AUG 5
TRASH PICKED-UP EARLY
MORNING

NO TRASH SERVICE

JULY 22: 100-104 VIA MALAGA
JULY 29: PLAZA CABANA

UPDATED
DUE TO CONSTRUCTION
LOGISTICS

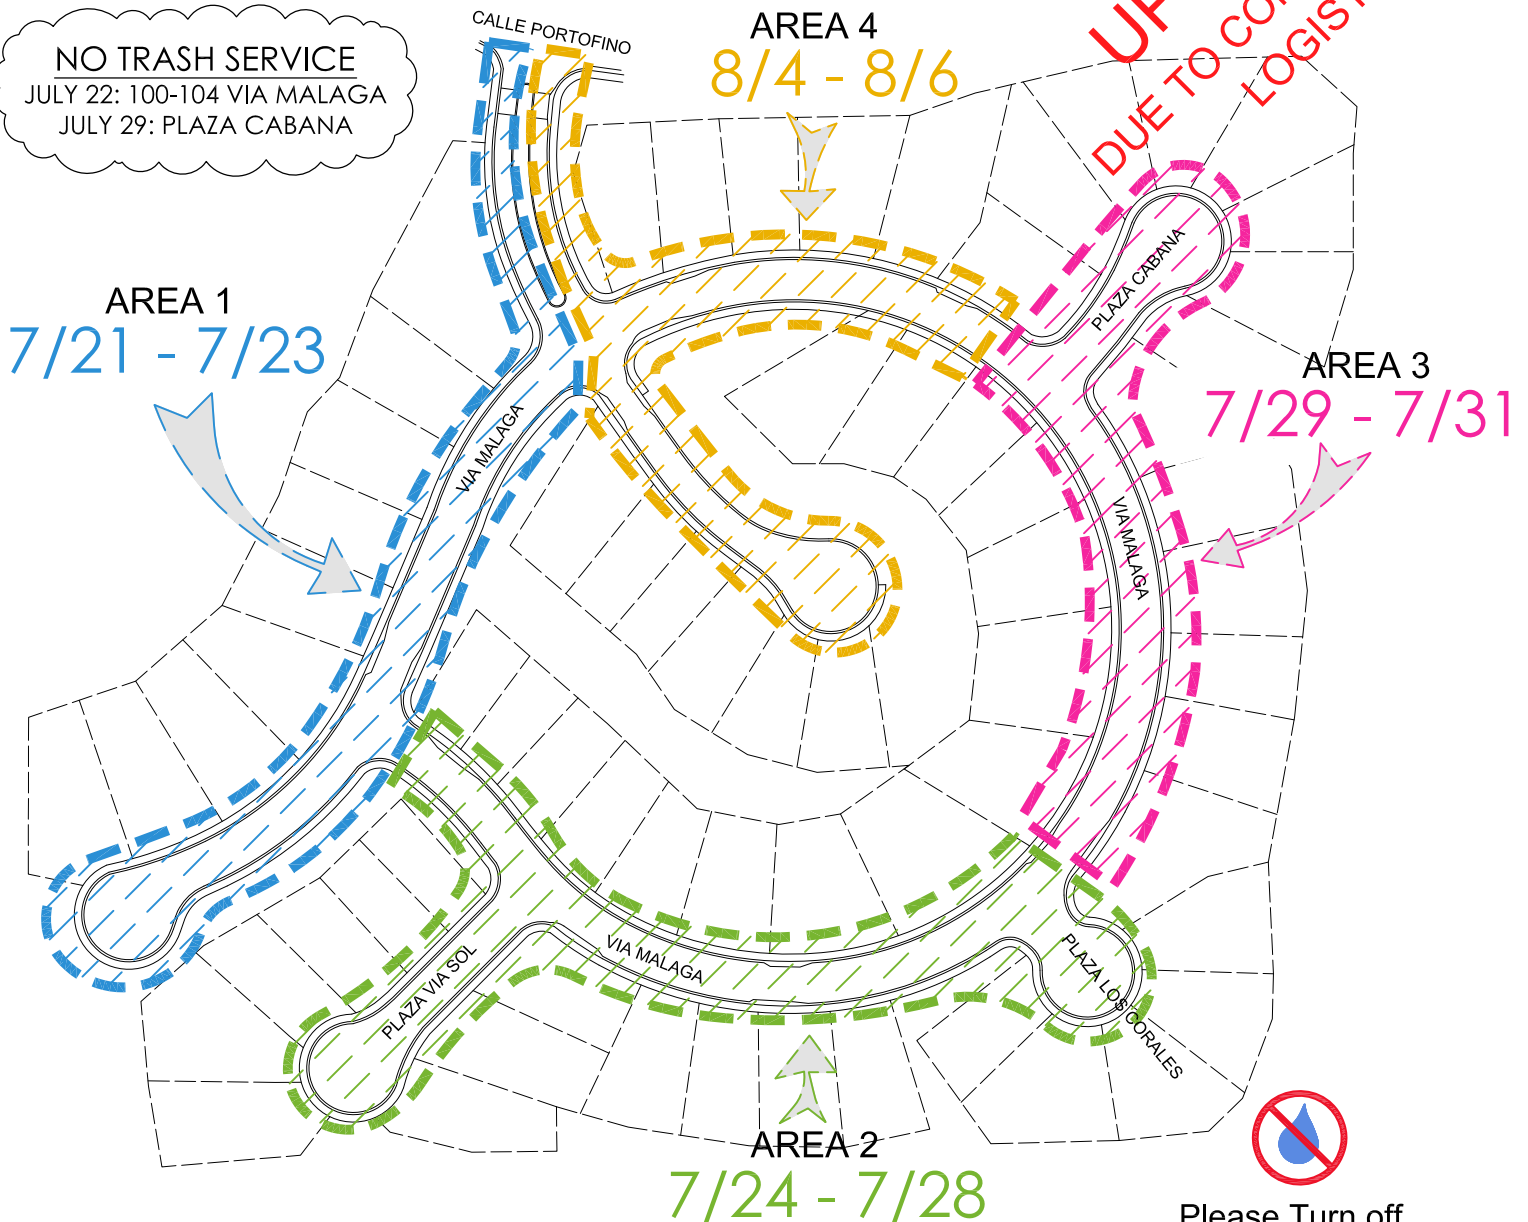

Please Turn off

Sprinklers/Irrigation during Scheduled Construction

HAND WATER IS PERMITTED

STREET CLOSURES



AREA 1	DATE	Daily Work Schedule
MON.	7/21	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	7/22	CLOSED 7:30 AM to 6:00 PM (PAVING)
WED.	7/23	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 2	DATE	Daily Work Schedule
THURS.	7/24	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
FRI.	7/25	CLOSED 7:30 AM to 6:00 PM (PAVING)
SAT-SUN	7/26-27	OPEN TO VEHICULAR TRAFFIC - PROCEED W/ CAUTION
MON.	7/28	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 3	DATE	Daily Work Schedule
TUES.	7/29	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
WED.	7/30	CLOSED 7:30 AM to 6:00 PM (PAVING)
THURS.	7/31	CLOSED 7:30 AM to 6:00 PM (PAVING)



AREA 4	DATE	Daily Work Schedule
MON.	8/4	CLOSED 7:30 AM to 6:00 PM (MILLING/DEMO)
TUES.	8/5	CLOSED 7:30 AM to 6:00 PM (PAVING)
WED.	8/6	CLOSED 7:30 AM to 6:00 PM (PAVING)

All of your vehicles should be moved out of the area prior to the start of construction daily. This means if you need to use your vehicle that is parked in your garage or driveway, it must be moved out of the area prior to 7:30 a.m. and may not return until the barriers are removed by the contractor.

AREAS OF CONSTRUCTION SHALL BE POSTED 72 HOURS IN ADVANCE

Your cooperation and patience during the construction activities is sincerely appreciated.

PLEASE LOCATE YOUR VEHICLE OUTSIDE WORK ZONES DURING SAID DATES

Plans Prepared By:
7/16/25



Project Engineer:
LaBelle Marvin, Inc.

PAVING CONTRACTOR
CHAMPION PAVING
